


Grizzly Flats Water System Restoration Schedule

As of March 7, 2022

| Water System Assessment | | Phase I: Restore NP Water to Gravity System | | Phase II: Address Wa Contamination Conc |
|---|----------------|--|----------------------|--|
| Visual Inspection of System 8/19/21-9/15/21 | 100% | Restore Reservoir Supply Line at Metering St 8/20/21-8/20/21 | ation 100% | Source Water Intake Modifications 9/13/21-3/15/22 |
| Isolate and Pressurize Gravity System 8/20/21-11/15/21 | | Restore Reservoir Supply Lines above Meter Station (@ Big Canyon) 9/24/21-11/20/21 | | Cap Services to Destroyed Structures 9/6/21-2/1/22 |
| Isolate and Pressurize Pressure System 9/20/21-2/8/22 | 100% | Restore Water Treatment (manual) 8/20/21-8/25/21 | 100% | Test System Water Quality Per DDW P 10/10/21-11/20/21 |
| Assess Surface Water Pipeline | 100% | Restore Water Treatment (automated) | 100% | |
| 9/1/21-6/15/22 | 15% | 8/25/21-1/15/22 | 90% | |
| Report on System Damage/Repair Recomm 9/20/21-9/27/21 | endations 100% | Restore Remote Monitoring of Treatment 8/25/21-9/8/21 | 100% | |
| | | Repair System Deficiencies (non-urgent leaks/r 10/1/21-6/1/22 | epairs) | |
| | | | 95% | |
| Restore Service to Pressure Zone | | Repair Surface Water Conveya System Damage | ince | Replace and Repai Non-Emergency System |
| nstall New Connection and Pumps 9/23/21-3/9/22 | 95% | Initial Repairs and Erosion Control Measures 9/27/21-10/25/21 | 100% | Repair Fire Hydrants 11/15/21-6/1/22 |
| Isolate and Test System, Repair Leaks 10/10/21-6/1/22 | | Replace Damaged Pipe and Appurtenances 4/15/22-6/15/22 | | Replace Pressure System Storage 9/1/22-12/1/22 |
| | 95% | | 0% | |
| | | Replace Metering Station 5/1/22-8/15/22 | | Replace Services 9/1/22-9/1/23 |
| | | | 0% | |



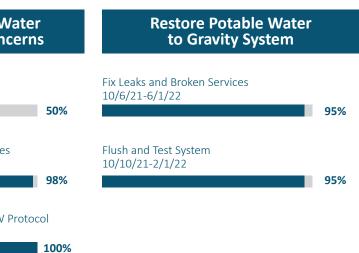



0%
